### Agenda



#### AGENDA

AGENDA ITEM	Presenter	START	DURATION
Call to Order	Co-Chairs	6:00 p.m.	5 min
Public Comment (2 mins per comment, max 10 mins)	Jada Simpson	6:05 p.m.	5 min
Approval of Minutes: January 14 , 2025	Co-Chairs	6:10 p.m.	5 min
Communications  Social Media / News Events  CAT & Community Meetings	Katy Fitzgold	6:15 p.m.	5 min
Finance - No February Presentation	Andre Andrews	N/A	0 min
Economic Opportunity Office  Engagement Outreach	Dinita Caldwell	6:20 p.m.	5 min
CMD 2022 Modernization/Comprehensive Projects     Drainage at Delco     Nelson Field parking     Oak Springs	Michael Mann & Program Managers	6:25 p.m.	20 min
CMD 2022 <u>Targeted</u> Projects	CMD Staff	6:45 p.m.	10 min
CMD Previous Bond Projects updates (2013 & 2017)	CMD Staff	6:55 p.m.	10 min
CBOC Committee Operations  Annual Report Approval  Letter to the Board Approval  Committee Operations Discussion	Co-Chairs	7:05 p.m.	50 min
Future Items for Discussion	Co-Chairs	7:55 p.m.	5 min
Adjourn	Co-Chairs	8:00 p.m.	
		555	

### **Public Comment**


All regular and plenary meetings of AISD advisory bodies are open to the public.


Members of the public may join CBOC meetings in-person and provide comments during the meeting or directly to the shared CBOC inbox before the meeting begins.

Email Address: <a href="mailto:cbocinternalinfo@austinisd.org">cbocinternalinfo@austinisd.org</a>

Five minutes of Public Comment may be read (maximum of 10 mins depending on sign-ups, no more than 2 mins per comment).



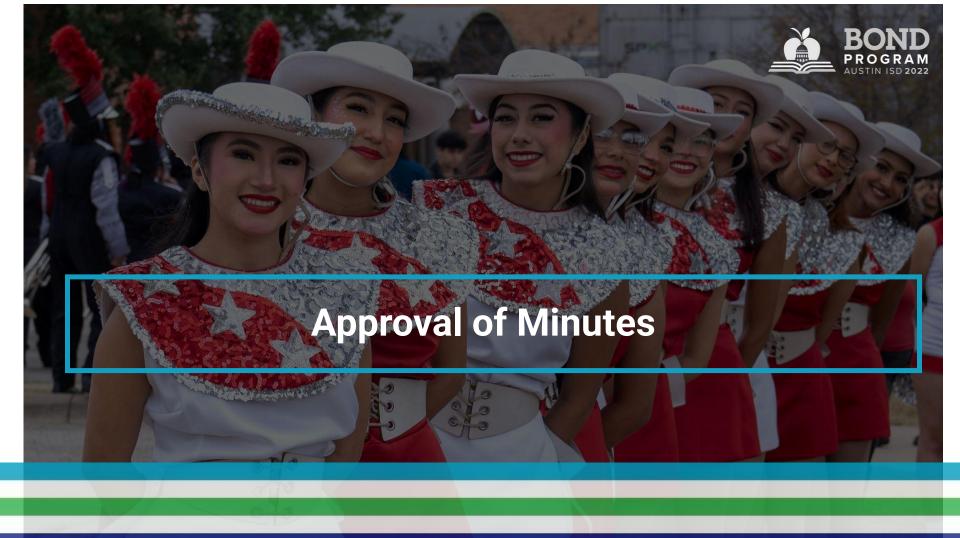

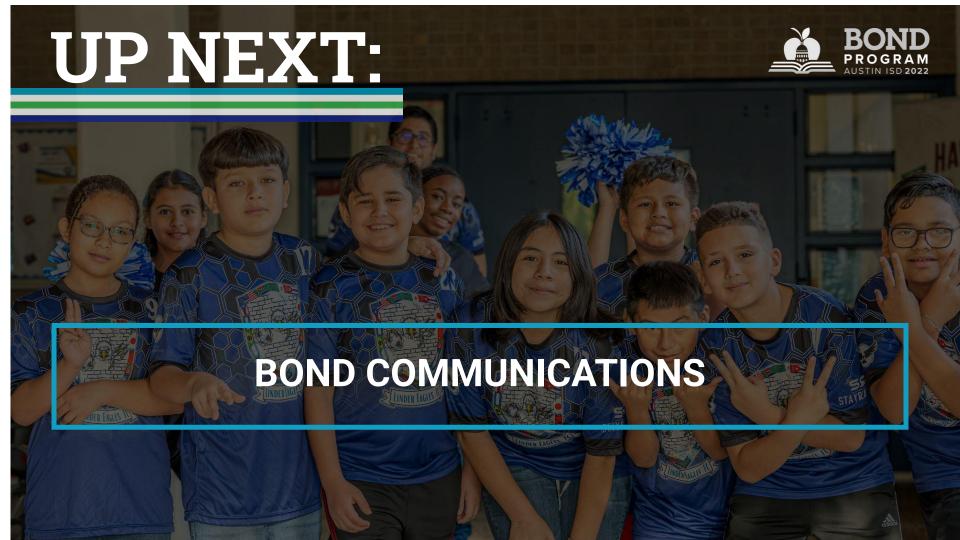

### **Austin ISD Bond Media Highlights**

We're keeping the community updated on the ongoing bond progress through news stories and social media posts. Check out the latest below.

#### **Social Media**

- Harris Construction
- CapMetro Partnership

#### **News Stories**

- McCallum Turf KVUE
- Pecan Springs Groundbreaking
  - o <u>KXAN</u>
  - o <u>KVUE</u>
  - Community Impact





### **Groundbreaking Events**

- March 4, 2025: Northeast Early College High School and International High School, 10 a.m.
- March 12, 2025: LBJ Early College High School, Time TBD
- March 13, 2025: Langford Elementary School, 1:30 p.m.





### **Community Meetings**

- February 5, 2025: Northeast Early College High School and International High School, 5:30pm\*
- February 26, 2025: LBJ Early College High School, 5:00pm\*
- March 11, 2025: Dobie Middle School, 5:30pm\*
- March TBD: Barrington Elementary School\*

All meetings are open to the public and posted to the Bond calendar.






<sup>\*</sup> Indicates a construction community meeting

### **CAT Meetings**

- January 23: Andrews Elementary School CAT Kick-Off
- January 31: O. Henry Middle School CAT form closed.
- February 3: Wooldridge Elementary School, 3:45 p.m.
- February 6: Central Athletic Facilities, 10:15 a.m.
- February 6: Andrews Elementary School, 4:15 p.m.
- February 7: Clifton Career Development School, 8 a.m.
- February 11: Langford Elementary School, 4:00 p.m.
- February 12: Austin High School 5:30 p.m.
- February 13: Nelson Bus Terminal, 11:00 a.m.
- February 13: Burnet Middle School, 4:30 p.m.
- February 19: O. Henry Middle School CAT Kick-Off, 4:30 p.m.
- February 19: Akins Early College High School, 5:00 p.m.
- February 20: Andrews Elementary School, 3:30 p.m.
- February 20: Barrington Elementary School, 3:30 p.m.
- February 24: Navarro Early College High School, 10:00 a.m.
- February 24: Wooldridge Elementary School, 3:45 p.m.
- February 26: Austin High School, 5:30 p.m.
- February 27: Clifton Career Development School, 8:00 a.m.

All meetings are open to the public and posted to the **Bond** calendar.

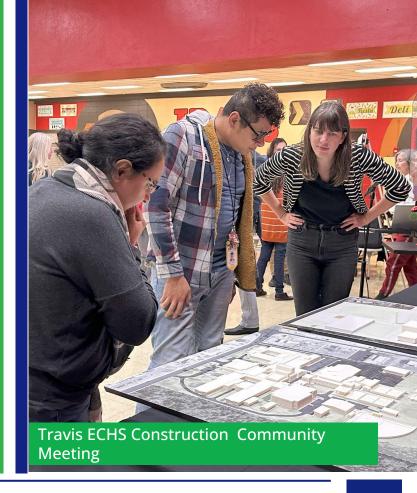





### 2013 Bond Financials



Bond amount authorized by voters on May 11, 2013: \$489,731,000

**Actually Spent** 

\$489,536,217

Total Projected Costs & Current Commitments

\$ 194,783

Bond Program
Available Balance
After Commitments

\$0

<sup>\*</sup>Please see file: 2013 Bond Program Financials

### 2017 Bond Financials



Bond amount authorized by voters on November 7, 2017: \$1,050,984,000

**Actually Spent** 

\$1,048,486,949

Total Projected Costs & Current Commitments

\$8,350,886

Bond Program
Available Balance
After Commitments

\$0

<sup>\*</sup>Please see file: 2017 Bond Program Financials

## 2022 Bond Financials Proposition A (General Purpose)



Bond amount authorized by voters on November 8, 2022: \$2,316,025,000

**Actually Spent** 

\$226,088,665

Total Projected Costs & Current Commitments

\$ 520,026,551

Bond Program
Available Balance
After Commitments

\$1,569,909,784

<sup>\*</sup>Please see file: 2022 Bond Program Financials

## 2022 Bond Financials Proposition B (Technology)



Bond amount authorized by voters on November 8, 2022: \$75,541,000

**Actually Spent** 

\$22,994,752

Total Projected Costs & Current Commitments

\$8,371,272

Bond Program
Available Balance
After Commitments

\$44,174,976

<sup>\*</sup>Please see file: 2022 Bond Program Financials

## 2022 Bond Financials Proposition C (Stadiums & Athletic Complexes)



Bond amount authorized by voters on November 8, 2022: \$47,434,000

**Actually Spent** 

\$250,656

Total Projected Costs & Current Commitments

\$ 2,290,557

Bond Program
Available Balance
After Commitments

\$44,892,787

<sup>\*</sup>Please see file: 2022 Bond Program Financials



### 2022 BOND PROGRAM - Architecture / Engineering: Through January 2025

Category	Contracted Amount (\$)	Paid Amount (\$)	Paid Progress	Paid Participation	HUB Goal (20%)
African American	9,620,921.58	3,296,555.53	34.3%	8.80%	3.0%
Asian/Native American	7,563,971.55	3,743,944.98	49.5%	10.0%	4.5%
Hispanic	12,140,986.48	2,653,972.26	21.9%	7.1%	4.7%
Women-Owned	2,550,923.70	558,664.33	21.9%	1.5%	7.8%
HUB Total	31,876,803.31	10,253,137.10	32.2%	27.3%	20.0%
Non-HUB	84,784,138.26	27,301,042.48	32.2%		
Total	116,660,941.57	37,554,179.58	32.2%		



Note: Adjusted HUB goals are derived from the 2022 Disparity Study.

### 2022 BOND PROGRAM - Construction: Through January 2025

Category	Contracted Amount (\$)	Paid Amount (\$)	Paid Progress	Paid Participation	HUB Goal (20%)
African American	1,982,197.00	1,571,597.75	79.3%	3.3%	3.5%
Asian/Native American	4,448,160.12	2,394,164.47	53.8%	5.0%	2.0%
Hispanic	7,496,409.18	4,394,159.47	65.8%	10.4%	4.7%
Women-Owned	8,434,249.28	4,351,706.57	51.7%	9.2%%	7.8%
HUB Total	22,361,015.28	13,256,644.82	59.3%	28.0%	18.0%
Non-HUB	85,434,369.45	34,170,648.79	40.0%		
Total	107,795,385.03	47,427,293.61	44.0%		



Note: Adjusted HUB goals are derived from the 2022 Disparity Study.

### **Economic Opportunity Office Outreach**



### **January 2025 Highlights**

- Thought-Provoking Thursday "Competitive Sealed Proposal Process" webinar featuring Bond Procurement and Construction Management - 36 businesses attended.
- EOO supported the Construction Management Vendor Info Session - 40+ attendees, 5 direct business contacts made, attendees represented 29.2% General Contractors, 12.5% Subcontractors, 51.2% Architects/Engineers, 6.2% other.
- EOO provided training and shared AISD procurement opportunities to over 40 small businesses for the Economic Growth Business Incubator.

### **Economic Opportunity Office Outreach**



January/2025

Year-to-Date

7

63

**Total Outreach Events** – HUB business expos hosted by external organizations, EOO organized HUB events, pre-bid meetings, and CAT meetings.

10

459

**Business Development Contacts** – Business and community stakeholder contacts made at business outreach events that lead to bidding opportunities for HUBs or that are directed to other internal departments for consideration.

9



**HUB Vendor Technical Assistance** – Business and industry organization meetings to include contractor associations and certification entities to facilitate future HUB forums, capacity building, and capability statement reviews.





## **UP NEXT:**

# 2022 BOND MODERNIZATION PROJECTS

Negotiations	Pre-Design	Schematic Design	Design Development	Construction Documents	Construction
<ul> <li>▲ Bear Creek ES</li> <li>(A)</li> <li>▲ Hill ES (A)</li> <li>▲ O. Henry MS (A)</li> </ul>	<ul> <li>Yellow Jacket         Stadium (A)</li> <li>Nelson Bus         Terminal (A)</li> <li>▲ Andrews ES (A)</li> </ul>	<ul> <li>Langford ES (A)</li> <li>Navarro ECHS (A)</li> <li>Austin HS (A)</li> <li>Wooldridge ES A)</li> </ul>	<ul> <li>Delco Activity         Center (c)</li> <li>Nelson Field (c)</li> <li>Oak Springs ES         (A)</li> </ul>	A LBJ ECHS (A)  A Burnet MS (A)  A Barrington ES (A)  A Martin MS (A)  A Akins ECHS (A)  ◇ Anderson HS (A)  ◇ Crockett ECHS (A)  ◇ Clifton CDS (A)  ◇ Dobie MS (A)  ◇ McCallum (A)  ◇ Mendez MS (A)	<ul> <li>Travis ECHS (A)</li> <li>Houston ES (A)</li> <li>*Pecan Springs ES (A)</li> <li>*Wooten ES (A)</li> <li>*Cook ES (A)</li> <li>*Oak Hill ES (A)</li> <li>*Williams ES (A)</li> <li>*Harris ES (A)</li> <li>*Odom ES (A)</li> <li>*Linder ES (A)</li> <li>*Allison ES (A)</li> </ul>
ICON KEY				<ul> <li>Northeast ECHS</li> </ul>	
	. A   (B) Prop. B   (C) Prop. C			& International HS (A)	I VVLA (A)
- Program Managers: ▲ - Final GMP *	AECOM				

### **Contingency & Escalation Use Update**

### Current reporting for Prop A

Bond Program	Original Balance	Previous Balance (as of 12/30)	Current balance (as of 1/31)
Contingency	\$129,093,277	\$32,605,777	\$32,805,777
Escalation	\$270,516,395	\$135,274,525	\$130,274,574

#### **Escalation Usage:**

- Swing for Pecan Springs to Winn
- Linder change order
- Certification Associates
- Condemnation Fees
- Crockett Turf
- > Payroll

<sup>\*</sup>Note: Information presented here is intended to communicate recent needs for contingency and escalation funds and is not intended to be a substitute for the financial reports provided.

### **Contingency & Escalation Use Report**

Current reporting for Prop C

<b>Bond Program</b>	Original Balance	Previous Balance (as of 12/30)	Current Balance (as of 1/31)
Contingency	\$2,834,978	\$2,834,978	\$2,834,978
Escalation	\$5,669,955	\$5,669,955	\$5,669,955

Contingency Usage:


N/A

**Escalation Usage:** 

 $\rightarrow$  N/A

<sup>\*</sup>Note: Information presented here is intended to communicate recent needs for contingency and escalation funds and is not intended to be a substitute for the financial reports provided.

### Program-wide Challenges & Strategies

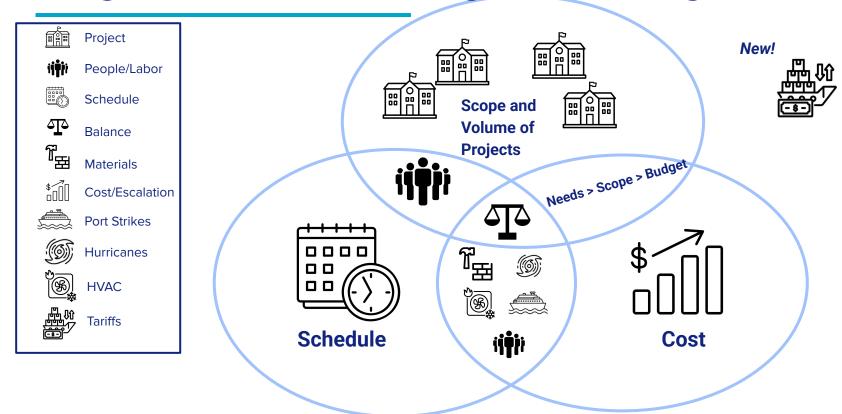

### **Program-wide Challenges & Strategies**

#### **Challenges**

- Internal staffing
- Limited City Staff for reviews, permitting and inspections
- Design community staffing limitations
- Construction community staffing limitations (GCs, Subs, Labor, etc.)
- Competition in the market
- Aggressive schedule
- Material availability
- Long-lead items
- Swing space
- Storm recovery efforts
- Port Strikes
- HVAC
- Tariffs



#### **Strategies**

- New accounting software
- New project management software
- Staff augmentation across multiple departments
- ILA with the City
- Developing new and improved SOPs
- Public Project Review Process
- Vendor & HUB Outreach
- Bundling projects
- Soliciting feedback from general contractors

### Delco Activity Center Drainage

Comprehensive | Prop. C



Scan the QR code to see the campus project page

**Project Fact Sheet** 

#### PHASE: DESIGN DEVELOPMENT | SCHOOL OPEN: JAN. 2028 | SWING: OFF-SITE | ON BUDGET: N

#### **Geotechnical Findings**

 Soil composition consists of high moisture content and fatty clay

#### **Drainage Survey Findings**

- Expansive soils are causing fluctuations to grading, leading to further drainage issues and water infiltration in the crawl space
- Crawl space drainage is malfunctioning, causing water to settle

#### **Structural Findings**

 Pooling water is causing upward force on structural piers, leading to movement of superstructure



Crawl Space Water Infiltration

### Delco Activity Center Drainage

Comprehensive | Prop. C



Scan the QR code to see the campus project page

**Project Fact Sheet** 


#### PHASE: DESIGN DEVELOPMENT | SCHOOL OPEN: JAN. 2028 | SWING: OFF-SITE | ON BUDGET: N

#### **Proposed Repairs Overview**

- Install concrete mud slab to properly capture any water infiltration
- Repair to crawlspace retention walls
- Install new drainage in crawl space
- Install new louvers, fans, & sensors to control humidity
- Regrade the perimeter of the building

#### **Next Steps**

Finalize design and recommendations

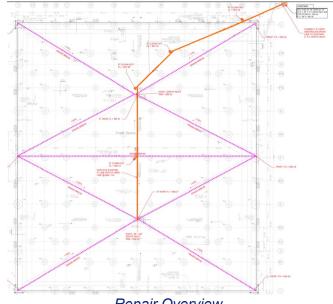

Repair Overview

### Nelson Field Parking

Comprehensive | Prop. C



Scan the QR code to see the campus project page

**Project Fact Sheet** 


#### PHASE: DESIGN DEVELOPMENT | PROJECT OPEN: JUN. 2026 | SWING: N/A | ON BUDGET: N

#### **Nelson Parking Update**

- A/E team has started analysis of Nelson parking.
- Nelson Bus design CATs will aid further coordination and prompt solutions.

#### **Parking Analysis**

- Avg. Home & Visitor Spectators 3,024
- Required Parking Stalls 1,008
- Current Home Stalls 549

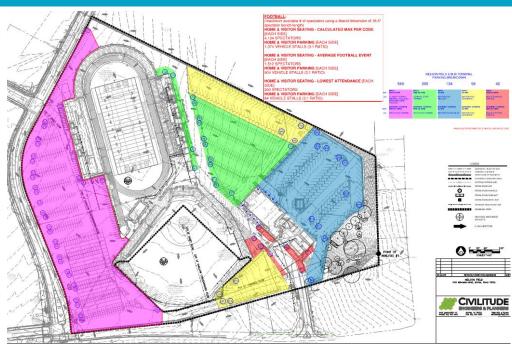

### Oak Springs Elementary

Full Modernization | Prop. A



Scan the QR code to see the campus project page

**Project Fact Sheet** 


#### PHASE: Construction Documents | SCHOOL OPEN: JAN. 2027 | SWING: IN-PLACE | ON BUDGET: N

#### **Project Highlights**

- Joint Use Park area will be rededicated after construction is completed
- Building & Site were redesigned during Schematic Design to preserve 39" Pecan Tree on the property
- The Team is evaluating options to reduce project costs without compromising Ed Spec requirements.




\*Conceptual renderings. Final design may vary.

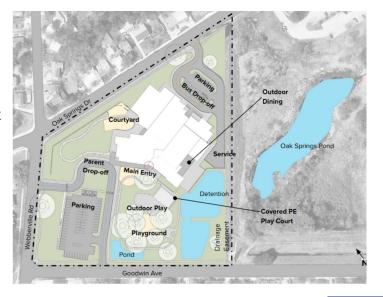



### **2022 Targeted Projects**

Prop A.

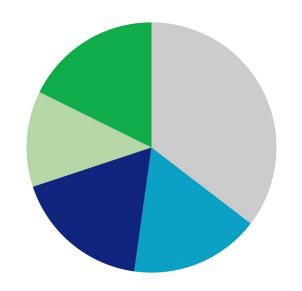

Approximate number of targeted projects = ~113\* \*Projects are bundled

- Remaining projects in queue (40)
- Pre-Design (19)
- Design (20)
- **Bidding (14)**
- **■** Construction (20)

#### **Targeted Descriptions**

- HVAC
- Building Repairs
- Safety & Security
- Roofing
- Artificial Turf Projects

### **Secure Entry Vestibules**

Prop A.

Construction on the first 28 projects is complete or nearly complete and the remaining 36 projects will take place in Summer 2025.






### **Additional Safety Projects**

Prop A.





### **2017 Bond Projects**

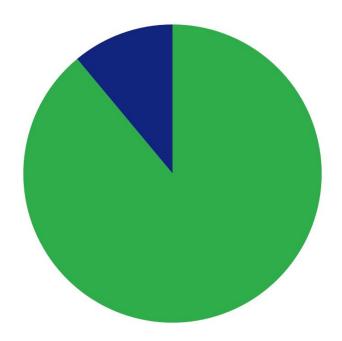

\*Please See File: 2017 Bond Projects


#### ■ 2017 Bond Projects Completed (153)

#### ■ 2017 Bond Projects Underway (11)

- Critical repairs (HVAC, electrical, plumbing, roofing, etc.) at various campuses
- House Park
- Life Safety projects at various campuses
- Demolish Pleasant Hill Annex

### **2013 Bond Projects**

- 2013 Bond Projects Completed (420)
- 2013 Bond Book Projects Underway (0)
- Interest Earned Funds & Surplus Projects (0)

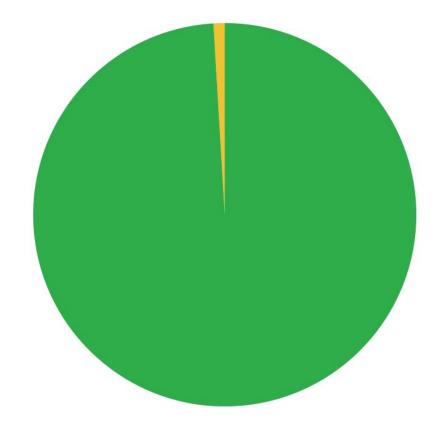

<sup>\*</sup>Please see file: 2013 Bond Projects



### **Committee Operations**

- Annual Report Approval
- Letter to the Board Approval
- Committee Operations Discussion
- Future Items for Discussion







